



# **Revised Opening Dates for Rail Transit Projects within Draft FY2017-2021 TIP and 2035 RTP**

**MAG MID PHASE PUBLIC MEETING**

**Wednesday, April 27, 2016**



# Future Transit Corridors



# Northwest LRT Extension Phase II

Project Complete	Current Phase	Phase Complete	Status
2023	Conceptual Engineering	Summer 2016	<ul style="list-style-type: none"> <li>Continue conceptual engineering</li> <li>Continue coordination with ADOT</li> <li>Initiate the Environmental Assessment and Preliminary Engineering in Summer 2016</li> </ul>

January 26, 2016 – Phoenix City Council votes to advance acceleration to 2023, from 2026.



# South Central

Project Complete	Current Phase	Phase Complete
2023	Project Development	Early 2017

## Status


- FTA approved entry into Project Development in November 2015
- Continue draft Environmental Assessment and preliminary engineering
- Submitted notification of intent to enter Engineering Phase to FTA

January 26, 2016 – Phoenix City Council votes to advance acceleration to 2023, from 2026.



# Capitol/I-10 West LRT Extension

<b>Project Complete</b>	January 26, 2016 – Phoenix City Council votes to split project into two phases, defer new Phase II until 2030.
<b>2023</b>	<ul style="list-style-type: none"> <li>Phase I ~ Central Avenue to 17<sup>th</sup> Avenue/Jefferson (1.5 miles)</li> </ul>
<b>2030</b>	<ul style="list-style-type: none"> <li>Phase II ~ 19<sup>th</sup> Avenue to 75<sup>th</sup> Avenue; via I-10 (9.5 miles)</li> </ul>

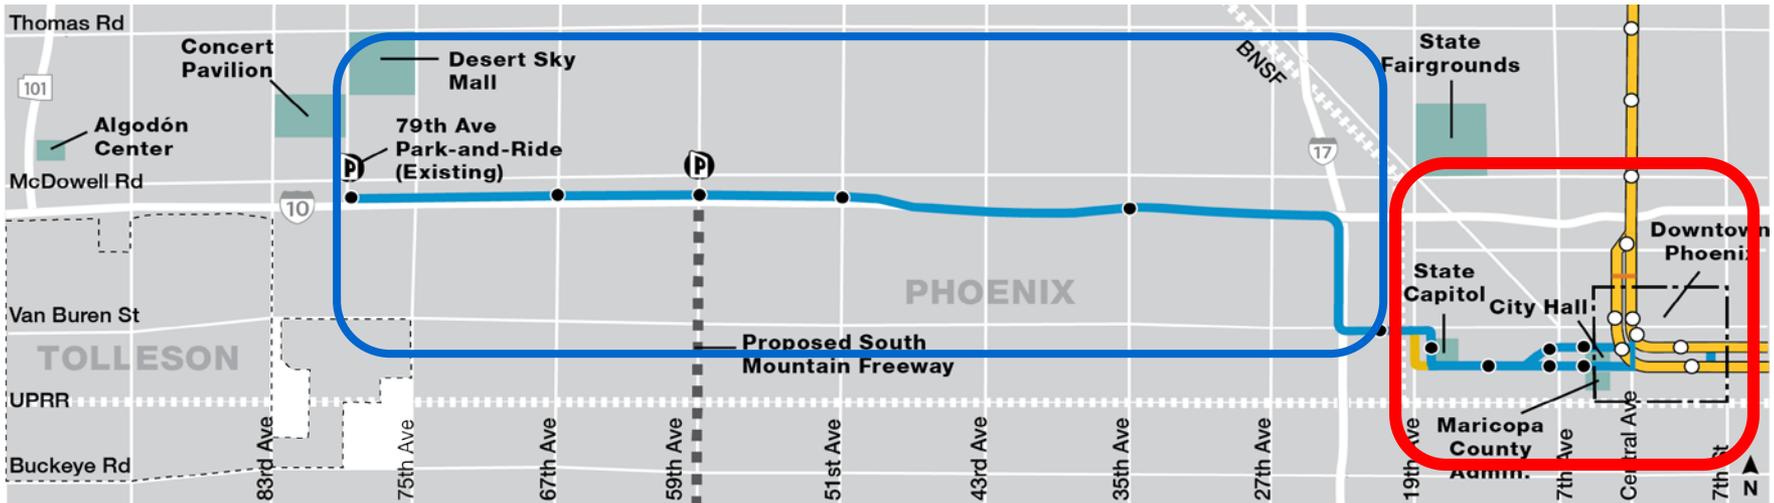

## LEGEND

-  Valley Metro Rail/Station
-  Proposed Station
-  McKinley St Turnaround Design Option
-  Build Alternative
-  Activity Center
-  City of Tolleson
-  Park-and-Ride
-  19th Ave North/South Design Option
-  Unincorporated Maricopa County

# Tempe Streetcar

Project Complete	Current Phase	Phase Complete	Status
2019 <i>(deferred one year from 2018, as per TLCP)</i>	FTA Project Development	Fall 2016	<ul style="list-style-type: none"> <li>■ Preliminary Engineering</li> <li>■ Initiating streetcar vehicle procurement</li> <li>■ Begin procurement of design, artist and CMAR in Summer 2016</li> </ul>



**Tempe Streetcar Project**  
3 miles

# 50<sup>th</sup> Street LRT Station

Project Complete	Current Phase	Phase Complete	Status
2019	Preliminary Engineering	Spring 2016	<ul style="list-style-type: none"> <li>Design, artist and CMAR procurement in Spring 2016</li> <li>Final Design begins Summer 2016</li> <li>Construction begins in Spring 2017</li> </ul>





**MARICOPA  
ASSOCIATION of  
GOVERNMENTS**



**VALLEY  
METRO**



**METRO**
