



**Agenda Item 5**  
**Alameda Drive Bicycle**  
**& Pedestrian Streetscape**  
**TMP19-740**  
**2<sup>nd</sup> Deferral Request**

**MAG Management Committee**


**September 16, 2020**



# Regional Context

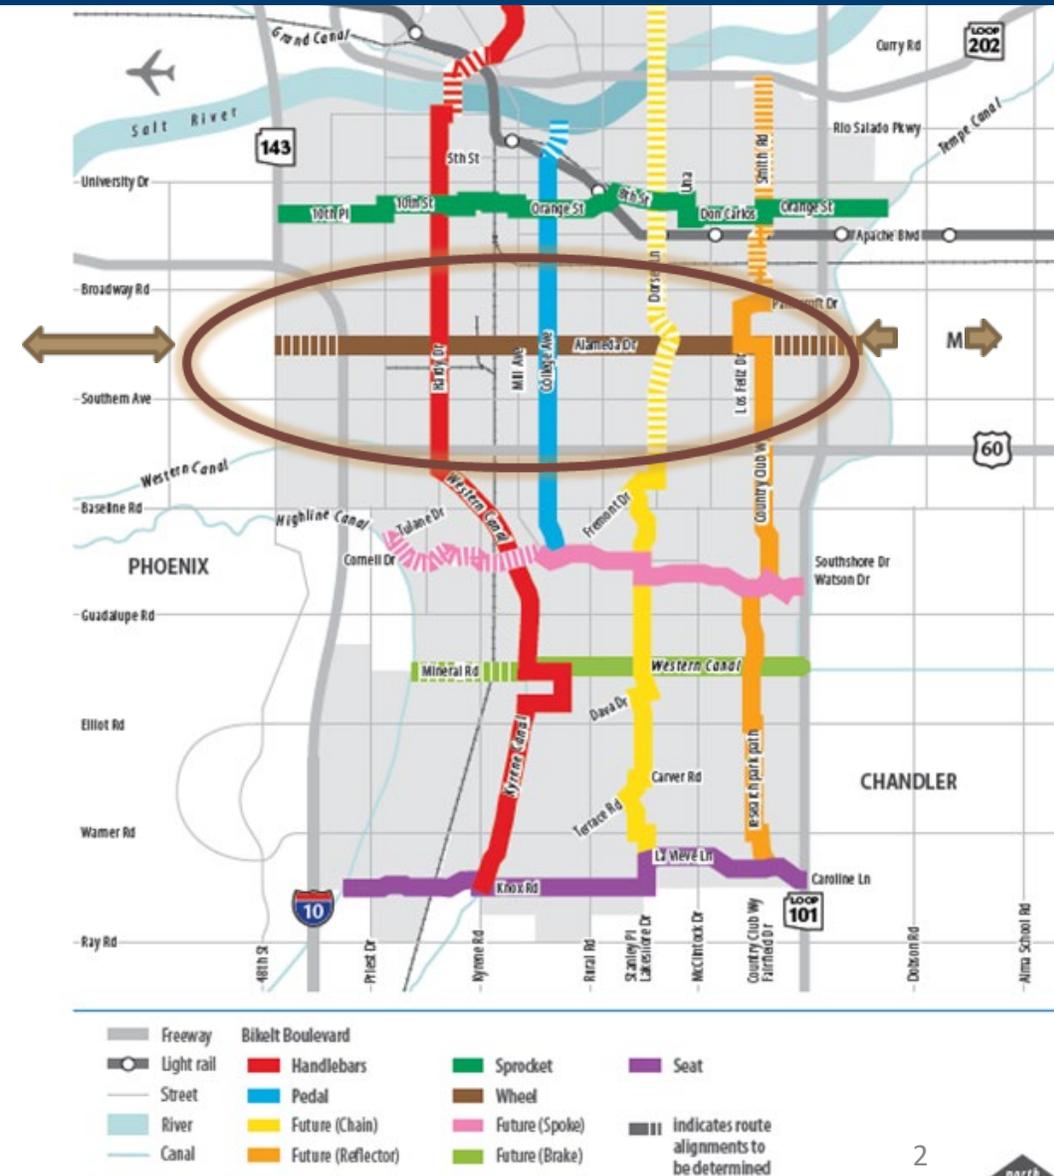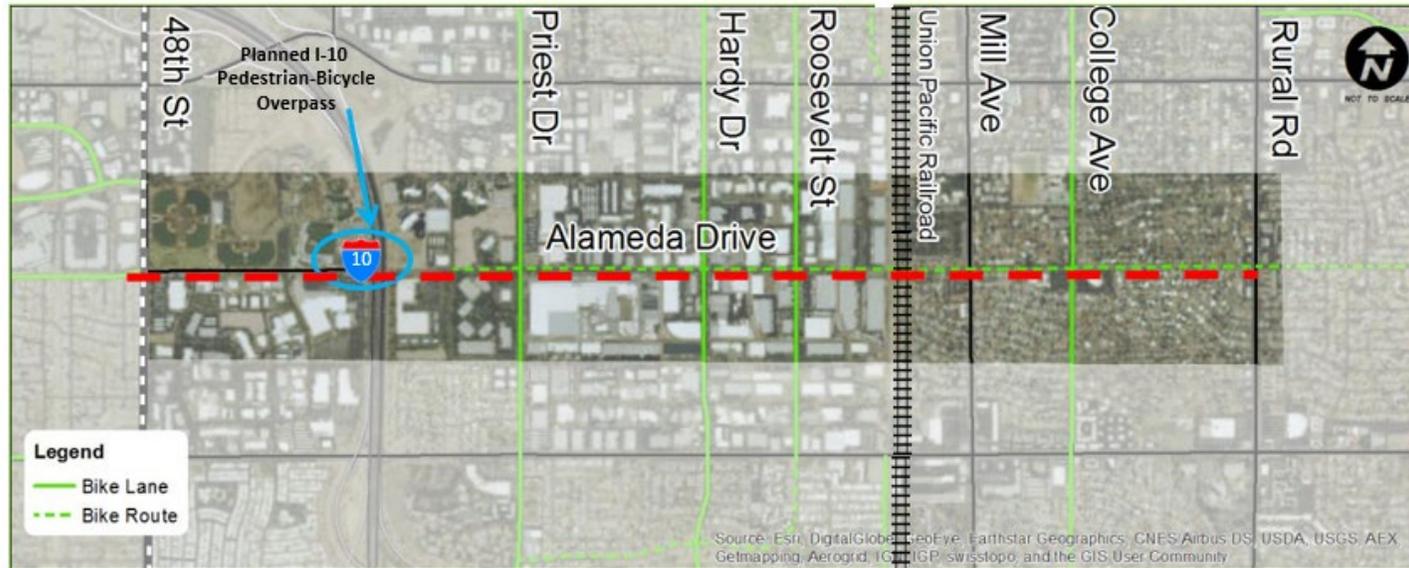

# Project Significance

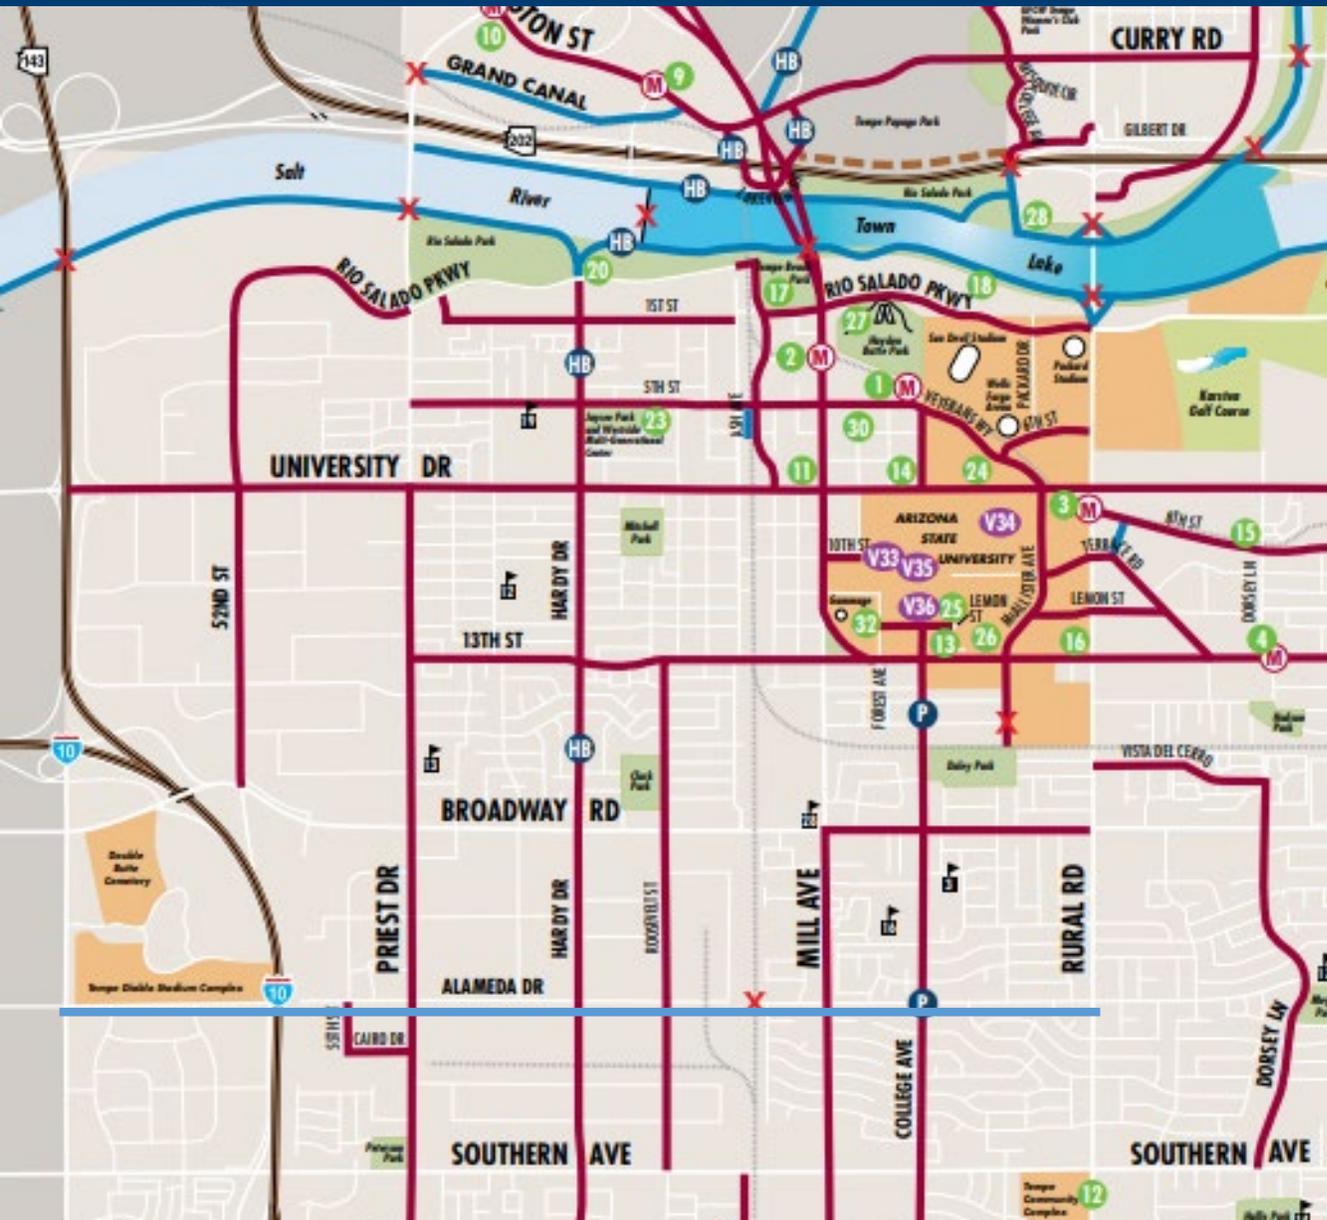

## I-10 Pedestrian-Bicycle Overpass

Arizona Department of Transportation (ADOT) is planning to construct a new pedestrian overpass connecting Alameda Drive on both sides of I-10.





# Project Summary



## 3-mile streetscape improvements

- Dedicated bike lanes throughout project limits
- UPRR Crossing Safety Improvements
- Landscaped medians & concrete-curb traffic calming bump outs
- Connection to new I-10 bike/ped bridge
- New sidewalks and ramps
- New pavement markings

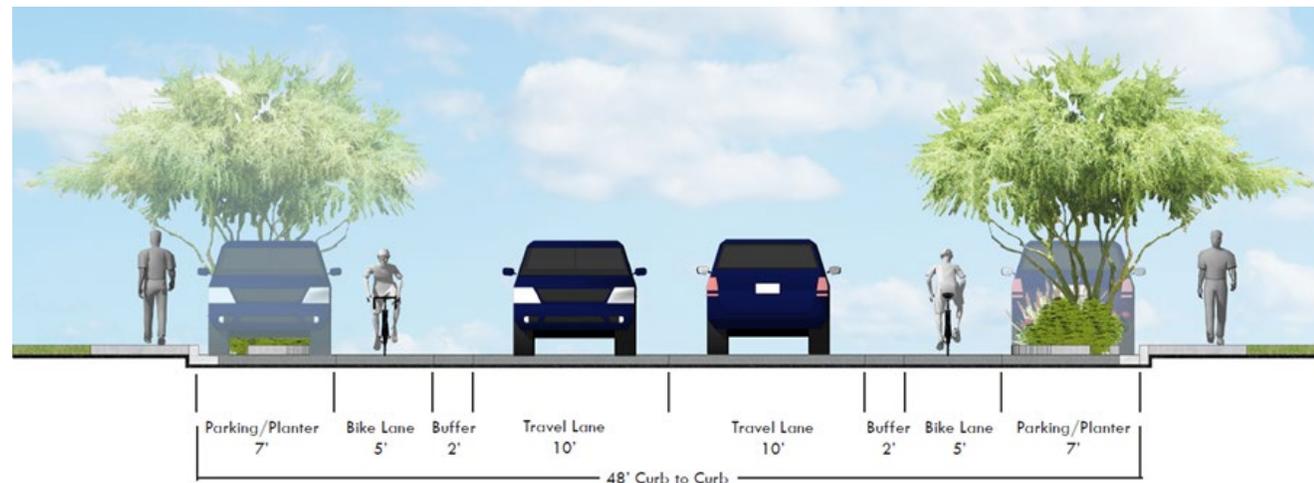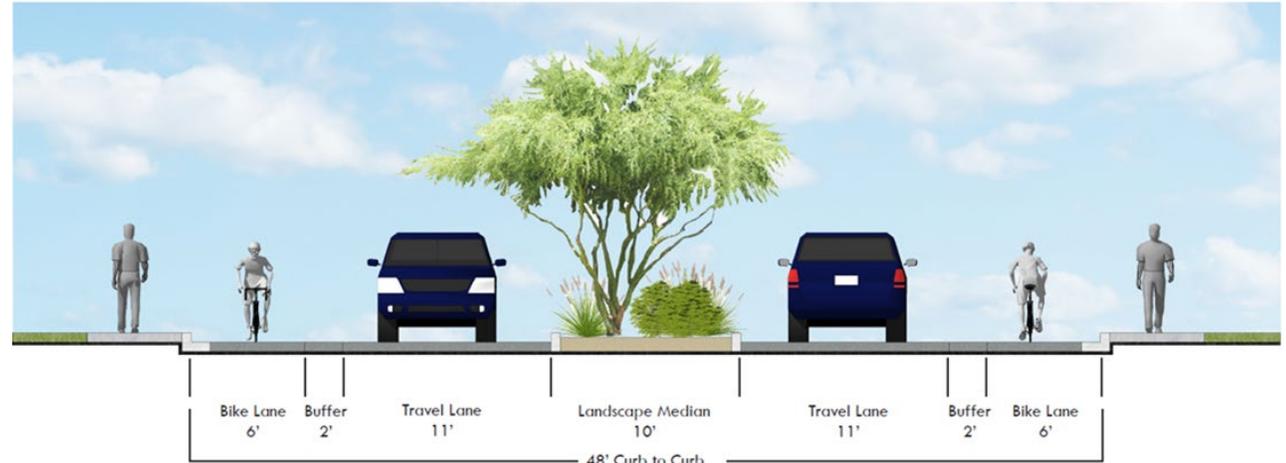

# Project Timeline



- **Awarded \$1,584,282 TAP Funding for FY2019 Construction**
- **Final Design started January 2018**
- **1<sup>st</sup> Deferral Requested April 2019 to move construction work phase from 2019 to 2020 due to waterline break, and coordinating/programming the re-location in Tempe's Capital Improvement Program.**
- **90% Final Design Completed February 2020**

# Current Deferral Request



Requesting approval of second deferral for the construction work phase for the Alameda Drive Bicycle and Pedestrian Improvement Project – Rural Road to 48th Street (TMP19-740) from FY20 to FY21:

- Coordination issues with Union Pacific Railroad for preliminary and final design of Alameda Railroad Crossing.
- Relocate and replace aging water line discovered during the design process at Alameda Drive between College Avenue and Mill Avenue.

# City Commitment



- Funding of \$1.5 Million is committed for water line design and construction.
- Additional \$200,000 funding for UPRR Crossing is programmed and committed for the Alameda Drive Bicycle and Pedestrian Improvement Project
- Project management staff is assigned through the completion of the project



# Next Steps



- UPRR Crossing Final Design: September 2020 – January 2021
- Water Line Final Design: August 2020 – January 2021
- Construction UPRR Crossing: January 2021 – March 2021
- Final Design Alameda Drive: December 2020 - March 2021
- Alameda Drive Streetscape Construction: May 2021- May 2022
- Water Line Construction: May 2021 – August 2021
- Questions?

